



MONTHLY CONSTRUCTION PROGRESS REPORT
 CITY OF SOUTH PASADENA
 PUBLIC WORKS DEPARTMENT

October 2016

**Preventative
 Maintenance Project**

Scope:


The work consists of slurry seal, cape seal, sawcut, removal and disposal of existing roadway sections, subgrade preparation and compaction, full depth asphalt concrete (AC) pavement, removal and reconstruction of damaged PCC curb and gutter, driveway approaches, reconstruction of localized failed asphalt concrete pavement areas, thermoplastic striping and pavement markings.

The limits of work include:

- Milan Avenue (from Monterey Road to Edgewood Drive)
- Maple Street (from Primrose Avenue to Stratford Avenue)
- Alpha Avenue (from Moffatt Street to Valley View Road)
- Valley View (from Alpha Avenue to Berkshire Avenue)
- Berkshire Avenue (Valley View Road to Valley View Road)
- Bank Street (from Freemont Avenue to Marengo Avenue)
- Huntington Lane (from Alhambra Road to Maple Street)
- Camino Lindo (from Alpha Avenue to Flores De Oro)

Details:

Bid Amount:	\$ 282,000
Extra Work to Date:	0
% Change to Contract:	0%
Amended Amount:	0
Total Contract Amount:	\$ 282,000
Construction Start:	Sept. 12, 2016
Duration:	80 Cal. Days
Orig. Completion Date:	Dec. 1, 2016
Est. Completion Date:	
Est. Percent Complete:	0

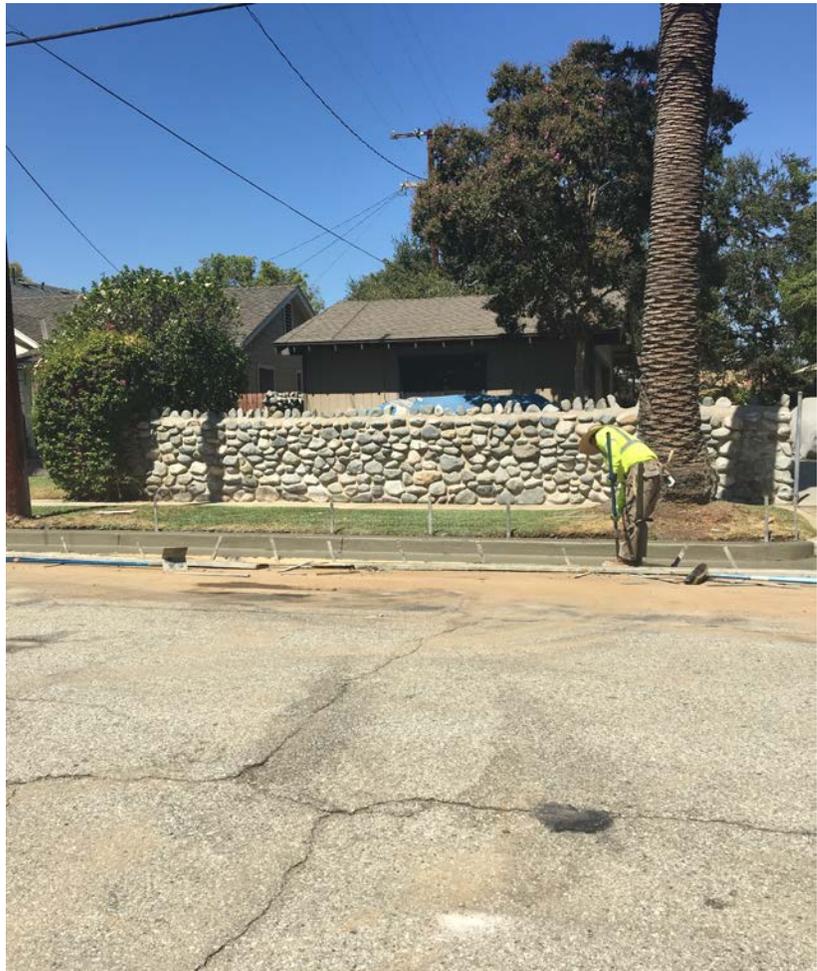

Status:

The contractor has completed all concrete work per construction plans. In the next several weeks, the contractor will begin to prepare road surface for crack seal and slurry seal treatments. The construction management and inspection services are being provided by GK & Associates and the contractor is Hardy & Harper, Inc.
